



Minnesota Street detour





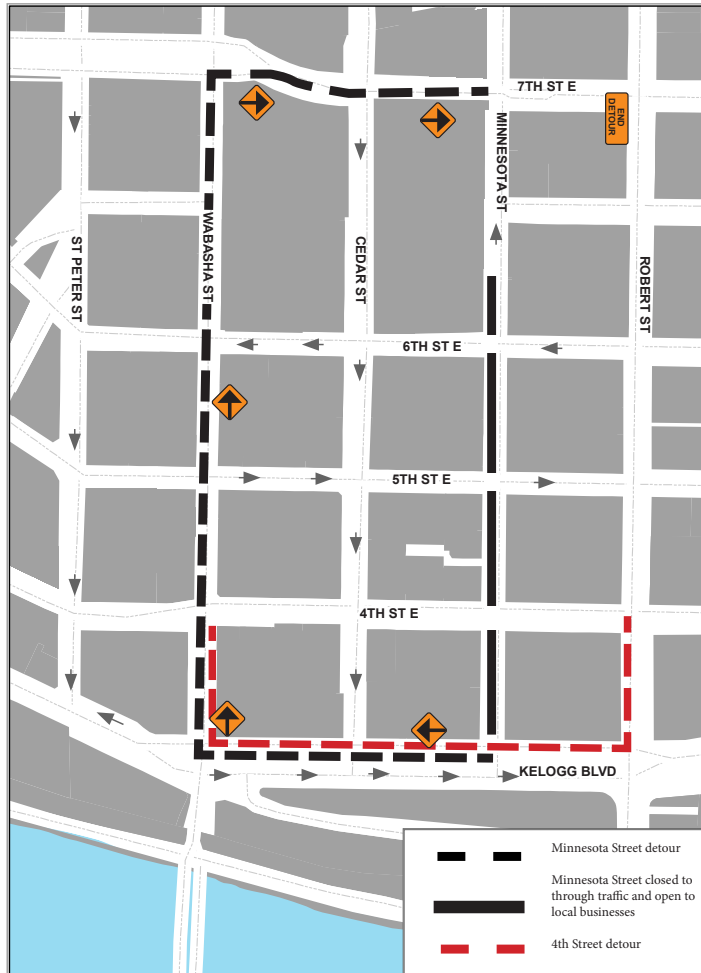

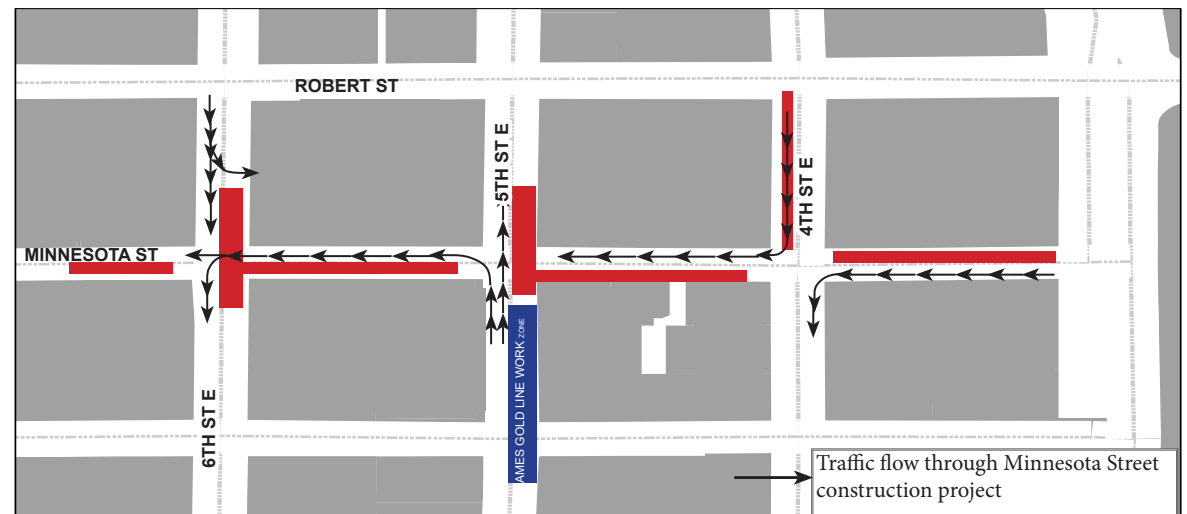







Access to local businesses on Minnesota



MINNESOTA ST & 4TH ST E- ST. PAUL CONSTRUCTION UPDATES:

Week of July 24,2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company, Inc. is currently working on pouring new storm sewer structures at the intersection of Minnesota Street and 4th Street. The crew is also installing piping between storm structures that are being constructed.
- The crew is working on the removal of the existing concrete road section as well as existing sidewalks at Minnesota Street between Kellogg Blvd. and 4th Street.
- Additional removal work took place between 4th Street and 5th Street for the installation of new storm sewer structures and piping.
- Pavers were removed at the Minnesota Street and 4th Street Intersection for upcoming concrete walk.
- Watermain installation was completed and the testing of the watermain took place on 7/20/2023.
- Several private utilities companies performed work on the project relocating their utility to allow for future project upgrades. These relocations are taking place at Minnesota Street between 4th Street and 5th Street. There are also relocations taking place at the 5th Street and 6th Street intersections.

MINNESOTA ST & 4TH ST E- ST. PAUL CONSTRUCTION UPDATES:

Week of July 24,2023



What's to Expect

- Veit & Company, Inc. will continue storm sewer installation at Minnesota Street and 4th Street as well as Minnesota Street between 4th Street and 5th Street.
- Veits street crew will start to grade and shape Minnesota Street between Kellogg Blvd. and 4th Street in preparation for new curb and gutter
- Curb and gutter will be installed at Minnesota Street between Kellogg Blvd. and 4th Street. Concrete paving may also take place if time allows.
- Watermain installation will take place on Minnesota Street between 4th Street and 6th Street. This night work will require a water shut-down. The watermain shut down is anticipated to take place on July 27th. Affected businesses will be notified with the hours of the shut down.
- Private utility work will continue on the project at Minnesota Street between 4th Street and 6th Street.
- Minnesota Street is closed to through traffic but will remain open to local business and parking ramps. We do not anticipate major changes to traffic control on the project. Access to businesses and parking ramps will remain the same.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
