



Minnesota Street detour





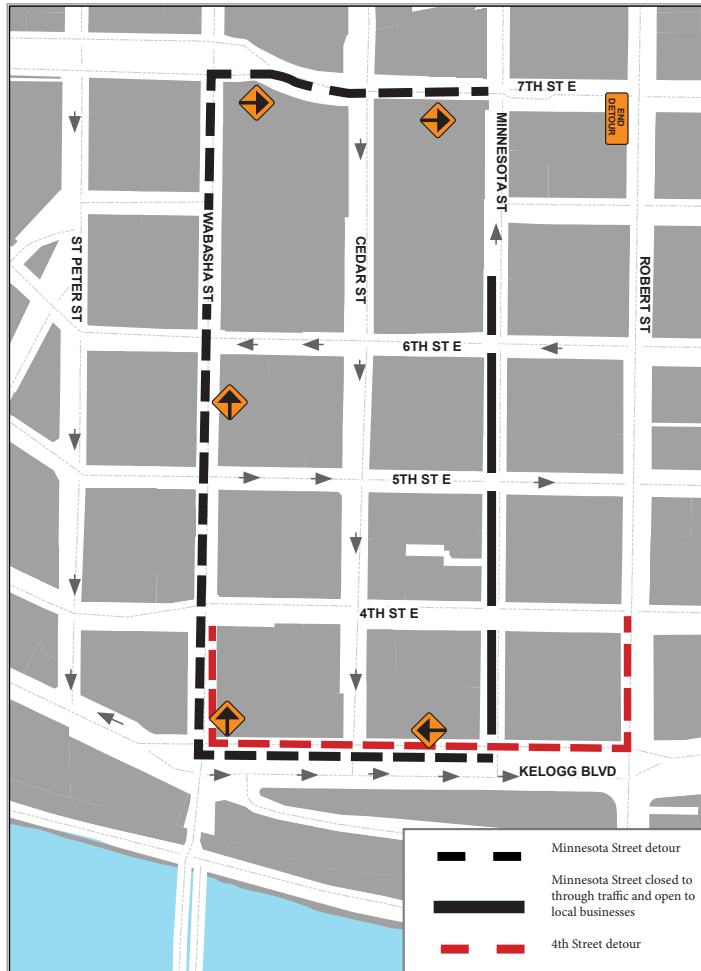

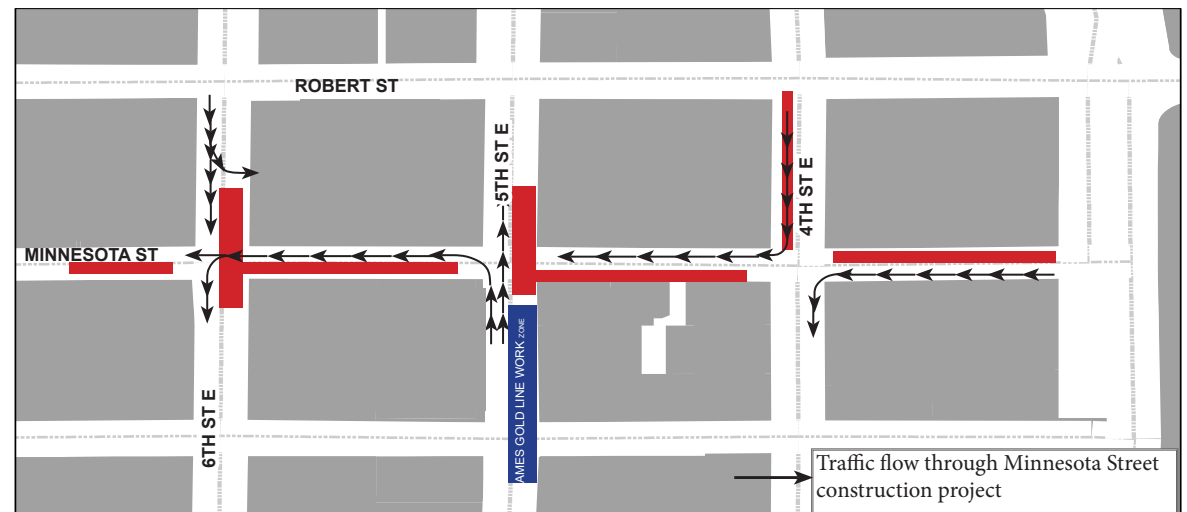









Access to local businesses on Minnesota



MINNESOTA ST & 4TH ST E- ST. PAUL CONSTRUCTION UPDATES:

Update for July 27,2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company, Inc. is currently working on pouring new storm sewer structures at the north side of the intersection of Minnesota Street and 4th Street. The crew is also installing piping between storm structures that are being constructed.
- The crew is working on the removal of the existing concrete sidewalks on Minnesota Street between Kellogg Blvd. and 4th Street.
- Veit & Company placed class 5 aggregate on Minnesota Street between Kellogg Blvd. and 4th Street in preparation for new concrete curb and gutter.
- Curb Masters was on site pouring concrete curb and gutter at Minnesota Street between Kellogg Blvd. and 4th Street.
- Veit & Company started to grade and tolerance the road section at Minnesota Street between Kellogg Blvd. and 4th Street in preparation for concrete paving.
- Additional removal work took place between 4th Street and 5th Street for the installation of new storm sewer structures and piping.
- Several private utilities companies performed work on the project relocating their utility to allow for future project upgrades. These relocations are taking place at Minnesota Street between 4th Street and 5th Street. There are also relocations taking place at the 5th Street and 6th Street intersections.

MINNESOTA ST & 4TH ST E- ST. PAUL CONSTRUCTION UPDATES:

Update for July 27,2023



What's to Expect

- Veit & Company, Inc. will continue storm sewer installation at Minnesota Street Between 4th Street and 5th Street.
- Veits street crew will complete the grading and shaping of Minnesota Street between Kellogg Blvd. and 4th Street to allow for new concrete paving.
- **Curb Masters will pour concrete pavement at Minnesota Street between Kellogg Blvd. and 4th Street.**
- **Curb Masters will pour concrete driveway aprons at Minnesota Street between Kellogg Blvd and 4th Street on Friday 7/28/2023. Access will be affected until Monday, July 31st. Businesses have been notified of this disruption to their access.**
- Veit & Company will grade for new sidewalks at the east and west sides of Minnesota Street between Kellogg Street and 4th Street.
- **Watermain installation will take place on Minnesota Street between 4th Street and 6th Street. This night work will require a water shut-down. The watermain shut down is anticipated to take place on July 27th. This shut down will happen between the hours of 6:30 pm to 11:30 pm. Affected businesses will be notified with the hours of the shut down.**
- Private utility work will continue on the project at Minnesota Street between 4th Street and 6th Street.
- Minnesota Street is closed to through traffic but will remain open to local business and parking ramps. We do not anticipate major changes to traffic control on the project. Access to businesses and parking ramps will remain the same.
- **A second night watermain shutdown will occur on August 3rd, 2023. The exact time has not been determined. Businesses will be notified and an update stating the times will be provided on this site on August 2nd, 2023.**

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
