
## MINNESOTA ST & 4TH ST E- ST. PAUL CONSTRUCTION UPDATES:

Week of July 17,2023





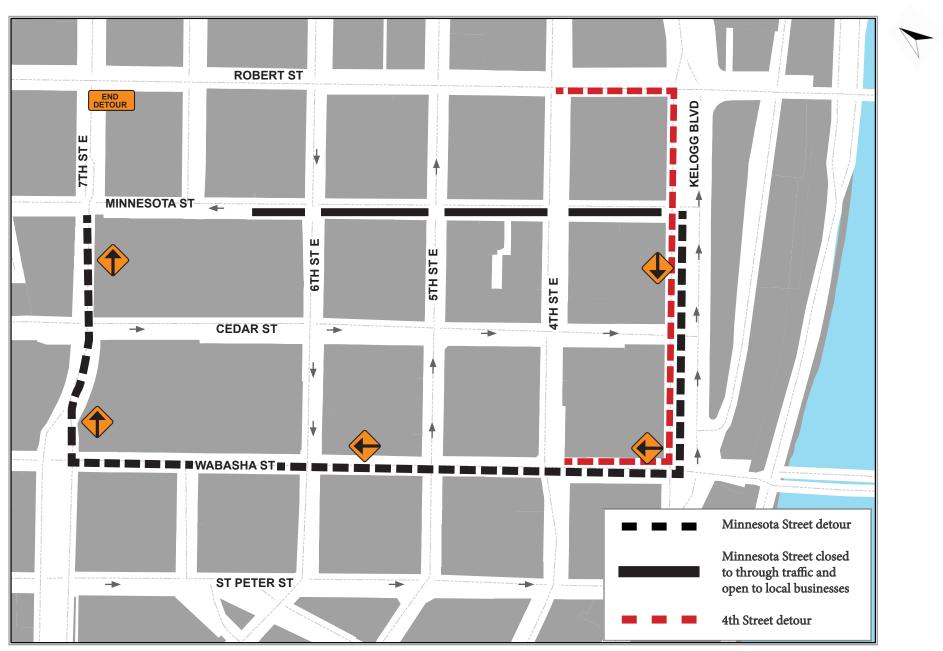

## MINNESOTA ST & 4TH ST E- ST. PAUL CONSTRUCTION UPDATES:

Week of July 17,2023

Block	Anticipated Construction Activities						Neter
	Sidewalk	Road	Storm Sewer	Signals	Removals	Underground Utilities	Notes
7th St to 6th St							
6th St Intersection							
6th St to 5th St					X		
5th St Intersection							
5th St to 4th St					X		
4th St Intersection							
4th St to Kellogg Blvd					X		



- Veit & Company, Inc. continued to work on various removals of concrete and bituminous throughout the project.
- •The crew excavated for the installation of watermain at Minnesota Street from Kelogg Boulevard to 4th Street.
- Bituminous Roadways (sub-contractor to Veit) pipe bursted the existing watermain to allow for a new watermain on Minnesota Street between Kellogg Boulevard and 4th Street.
- Additional signage was placed on the project to assist motorists with direction on how to traverse the project.
- Several private utilities companies performed work on the project relocating their utility to allow for future project upgrades. These relocations are taking place at Minnesota Street between 4th Street and 5th Street. There are also relocations taking place at the 5th Street and 6th Street intersections.






## MINNESOTA ST & 4TH ST E- ST. PAUL CONSTRUCTION UPDATES:

Week of July 17,2023



- Veit & Company, Inc. will continue watermain installation at Minnesota Street between Kellogg Boulevard and 4th Street. The crew will also install storm sewer at the intersection of Minnesota Street and 4th Street. Veits street crew will start to grade and shape Minnesota Street between Kellogg Boulevard and 4h Street in preparation for new curb and gutter.
- Private utility work will continue on the project at Minnesota Street between 4th Street and 6th Street.
- Minnesota Street is closed to through traffic but will remain open to local business and parking ramps. We do not anticipate major changes to traffic control on the project. Access to businesses and parking ramps will remain the same.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.

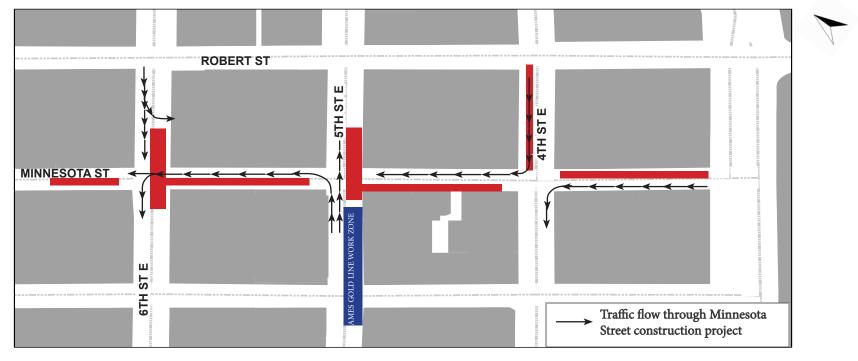

## Access to local businesses on Minnesota Street

