



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of August 28, 2023

Minnesota Street detour



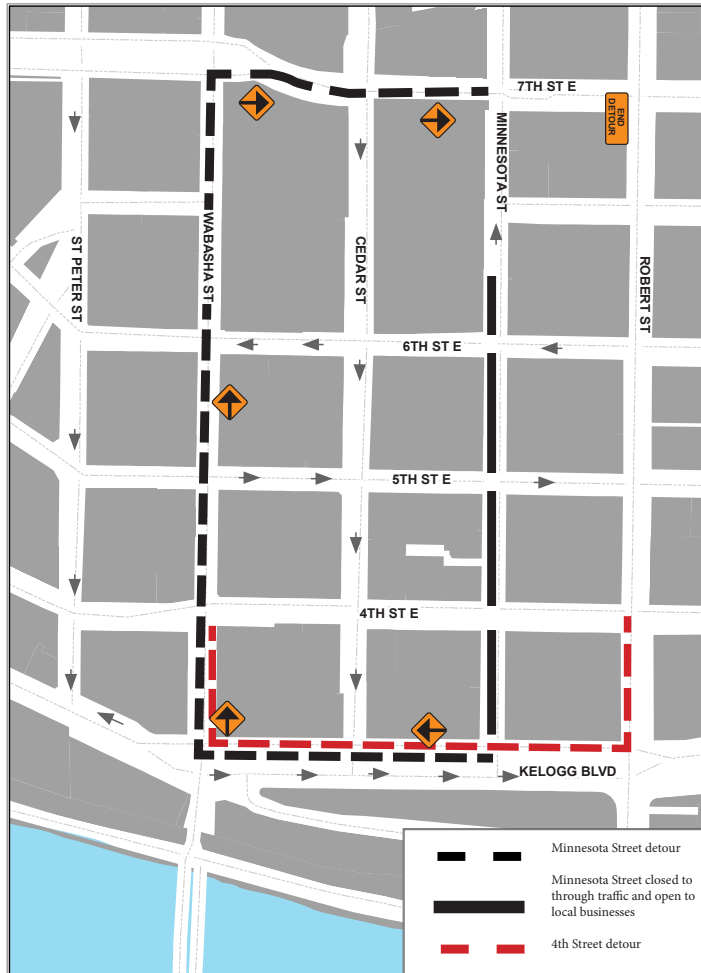

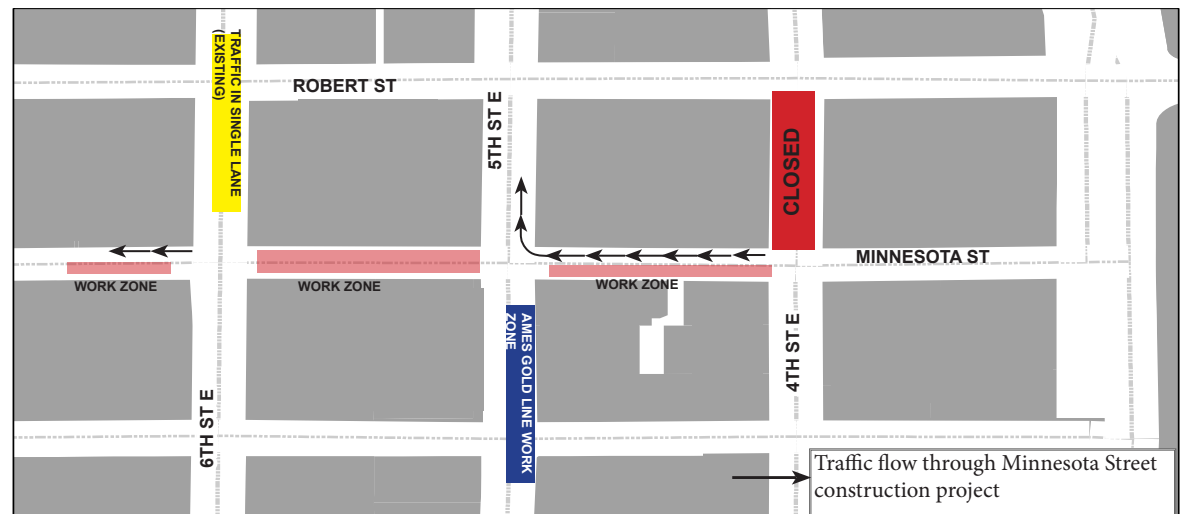








Access to local businesses on Minnesota



4th Street is currently closed between Minnesota Street and Robert Street

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of August 28,2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company utility crews are installing storm sewer structures and piping at the Minnesota Street and the 4th Street intersection
- Veit & Company utility crews also installed watermain at the north side of the Minnesota Street and 6th Street intersection.
- Veit & Company street crews are currently working on removing the existing concrete and bituminous road section at 4th Street, west of Minnesota Street.
- Veit & Company street crews are also working on completing the concrete street and sidewalk removals at the Minnesota and 6th Street intersection.
- Veit & Company street crews are working on grading and shaping Minnesota Street from 5th Street toward 6th Street in preparation for new concrete street paving.
- Curb Masters is pouring concrete curb and gutter at Minnesota Street between 5th Street and 6th Street.
- Several private utilities companies performed work on the project relocating their utility to allow for future project upgrades. These relocations are taking place at Minnesota Street between 5th Street and 6th Street.

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of August 28,2023



What's to Expect

- Veit & Company utility crews will complete the storm sewer installation at the Minnesota Street and 4th Street intersection .
 - Veit & Company street crew will start grading, shaping and placing class 5 aggregate at Minnesota Street between 5th Street and 6th Street.
 - Veit & Company street crew will also grade, shape and place class 5 aggregate at the Minnesota Street and 6th street intersection.
 - Curb Masters will pour concrete pavement at Minnesota Street between 5th Street and 6th Street.
 - Private utility work will continue on the project at Minnesota Street between 4th Street and 6th Street.
 - St. Paul Lighting will work on installing conduit for new lighting at the Minnesota Street and 6th Street intersection.
 - Minnesota Street is closed to through traffic but will remain open to local business and parking ramps. Please see the updated detour plan for changes in the coming week.
-
- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.
-
- We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
