



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of September 10, 2023

Minnesota Street detour



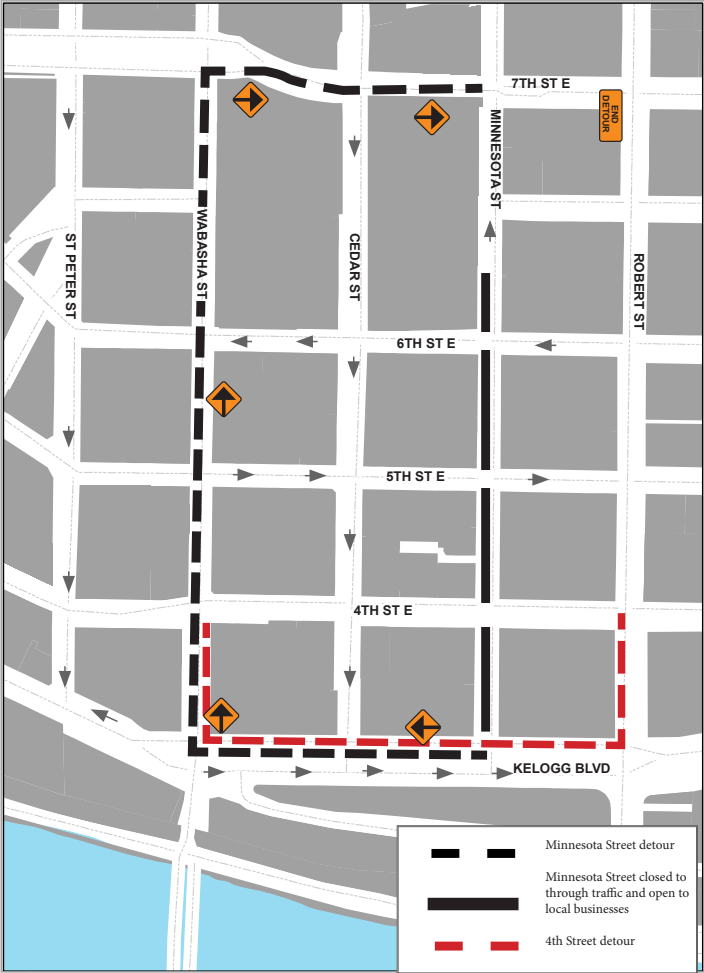

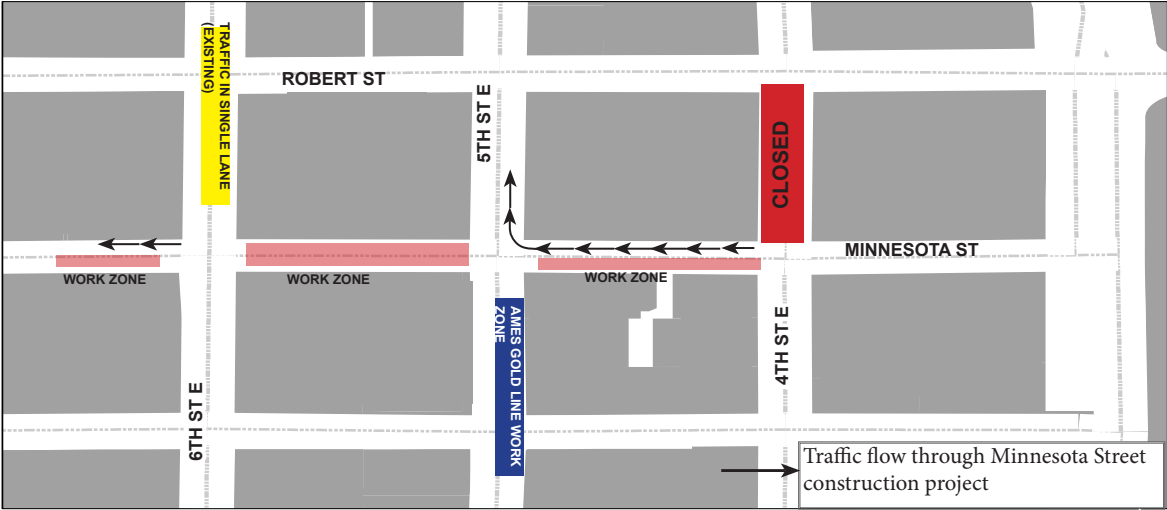







Access to local businesses on Minnesota



4th Street is currently closed between Minnesota Street and Robert Street



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of September 10, 2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company utility crews are completing the storm sewer and structure installations at the Minnesota St. and 4th St. intersection.
- Veit & Company street crews worked on completing the existing sidewalk removals at the west side of Minnesota Street between Kellogg Blvd. and 4th Street.
- Veit & Company street crew also worked on the removal of the existing sidewalks at Minnesota Street between 4th Street and 5th Street.
- Veit & Company street crew also graded and shaped class 5 aggregate in preparation for paving/patching at Minnesota Street between 4th Street and the 5th Street intersection.
- Curb Masters is pouring concrete pavement at the west side of Minnesota Street between Kellogg Blvd. and 4th Street.
- Curb Masters poured the concrete pavement at Minnesota Street from 5th Street toward 6th St. and the 6th Street intersection
- Light bases for new street lighting were installed at Minnesota Street between Kellogg Blvd. and 4th Street.
- Light bases and conduit were installed at Minnesota Street between 5th St. and 6th St.

Several private utilities companies performed work on the project relocating their utility to allow for future project upgrades. These relocations are taking place at Minnesota Street between 5th Street and 6th Street.

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: **Week of September 10,2023**



What's to Expect

- Veit & Company utility crews will install remaining storm sewer at Minnesota Street and 6th Street intersection as well as 6th Street west of Minnesota Street.
- Veit & Company utility crews will install storm drain tile on Minnesota Street between Kellogg Blvd. and 4th Street.
- Veit & Company street crew will complete the removal of the existing street section at the south side of the Minnesota Street and 6th Street intersection
- Veit & Company street crew will also grade, shape and place class 5 aggregate at Minnesota Street between 4th Street and 5th Street intersection.
- Veit & Company street crew will grade, shape and place class 5 aggregate at the intersection of Minnesota Street and 4th Street in preparation for pouring curb and gutter.
- Curb Masters will pour concrete sidewalk at Minnesota Street at the 4th Street intersection and continue north to the 5th Street intersection.
- Curb Masters will pour concrete pavement at Minnesota Street and the 4th Street intersection.
- Curb Masters will also pour concrete pavement at Minnesota Street between 4th St. and 5th St.
- Private utility work will continue on the project at Minnesota Street between 4th Street and 6th Street.
- Signal bases and conduit for the new signal at Minnesota St. and 6th Street intersection will be installed.

- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.

- We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
