



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of September 17, 2023

Minnesota Street detour



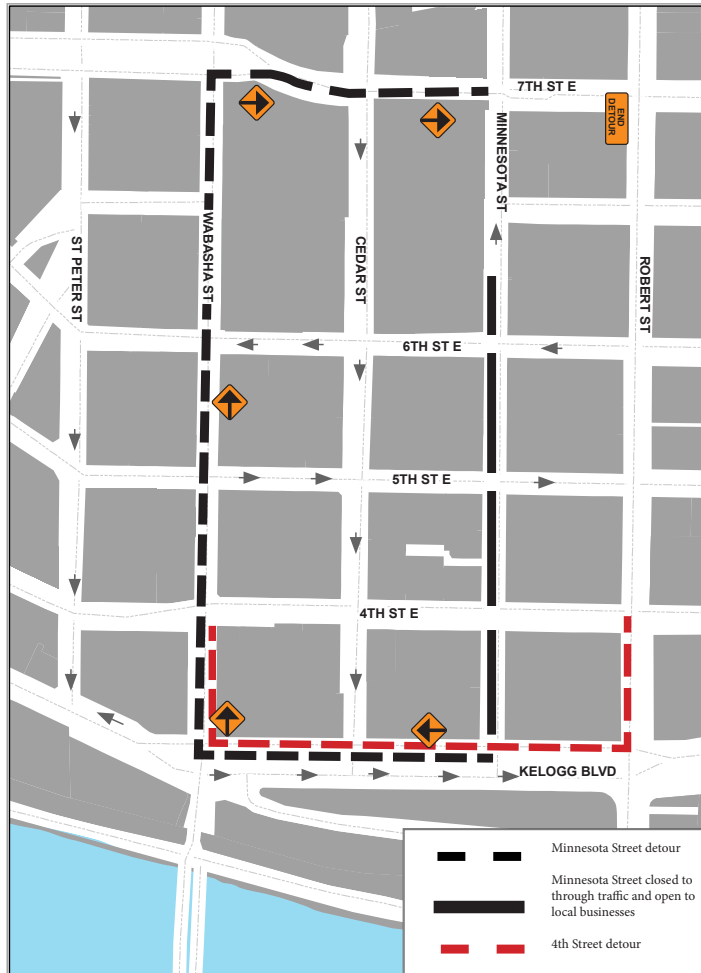

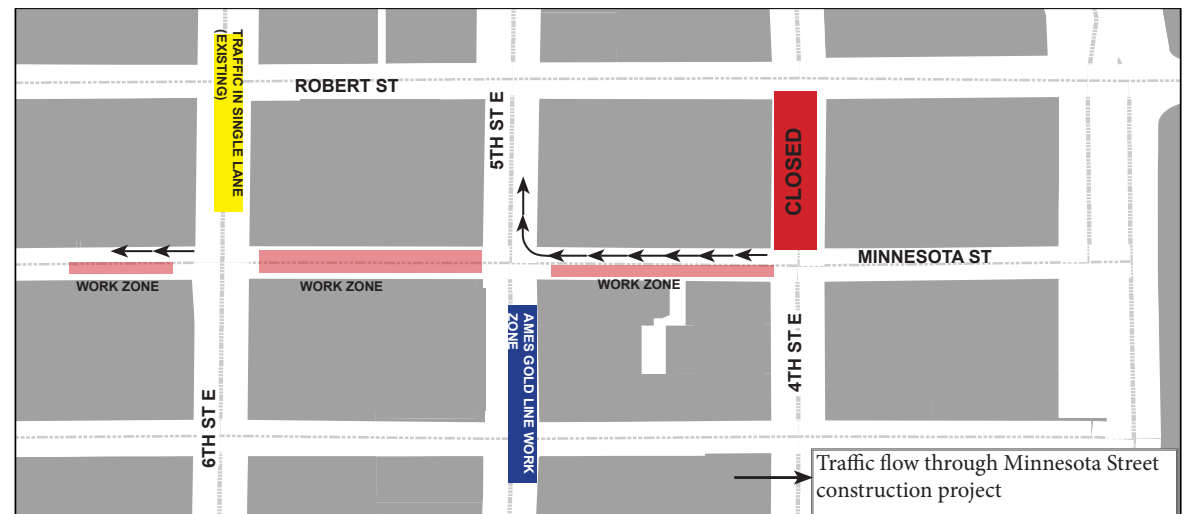










Access to local businesses on Minnesota



4th Street is currently closed between Minnesota Street and Robert Street

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of September 17, 2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company utility crews are completing the storm sewer drain tile at Minnesota Street between 4th Street and Kellogg Boulevard.
- Veit & Company utility crews are completing the storm sewer structures at Minnesota Street between 4th Street and 5th Street.
- Veit & Company utility crews also completed the storm sewer installation at Minnesota street between 5th Street and 6th Street.
- Veit & Company street crews are working on grading and shaping the road sections at Minnesota Street between 4th Street and the 6th Street intersection.
- Veit & Company street crews are performing removals of existing curb and gutter, sidewalk and streets at various locations at Minnesota Street between 4th Street and 6th Street.
- Curb Masters is pouring concrete pavement at Minnesota Street between 5th Street and 6th Street.
- Curb Masters poured concrete curb and gutter at Minnesota Street between 4th Street and 5th Street as well as the Minnesota and 4th Street Intersection and the intersection located at Minnesota Street and 5th Street.
- Light bases and conduit were installed at Minnesota Street between 5th St. and 6th St.
- Several private utilities companies performed work on the project relocating their utility to allow for future project upgrades. These relocations are taking place at Minnesota Street between 4th Street and 6th Street.

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: **Week of September 17,2023**



What's to Expect

- Veit & Company utility crews will install remaining storm sewer at Minnesota Street and 6th Street intersection as well as 6th Street west of Minnesota Street.
 - Veit & Company utility crews will install a new tree trench located at Minnesota Street between Kellogg Boulevard and 4th Street.
 - Veit & Company street crew will complete the removal of the existing street section at Minnesota Street between 4th Street and 5th Street.
 - Veit & Company street crew will also grade, shape and place class 5 aggregate at Minnesota Street between 4th Street and 5th Street intersection.
 - Veit & Company street crew will grade, shape and place class 5 aggregate at the intersection of Minnesota Street and 6th Street in preparation for new concrete curb and gutter and sidewalks.
 - Curb Masters will pour concrete sidewalk at Minnesota Street at various locations between 5th Street and the 6th Street intersection.
 - Curb Masters will pour concrete pavement at Minnesota Street north of 4th Street to 5th Street
 - Curb Masters will also pour concrete pavement at the intersection of Minnesota Street and 4th Street.
 - Private utility work will continue on the project at Minnesota Street between 4th Street and 6th Street.
 - Signal bases and conduit for the new signal at Minnesota St. and 6th Street intersection will be installed.
- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.
- We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
