



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of September 25, 2023

Minnesota Street detour

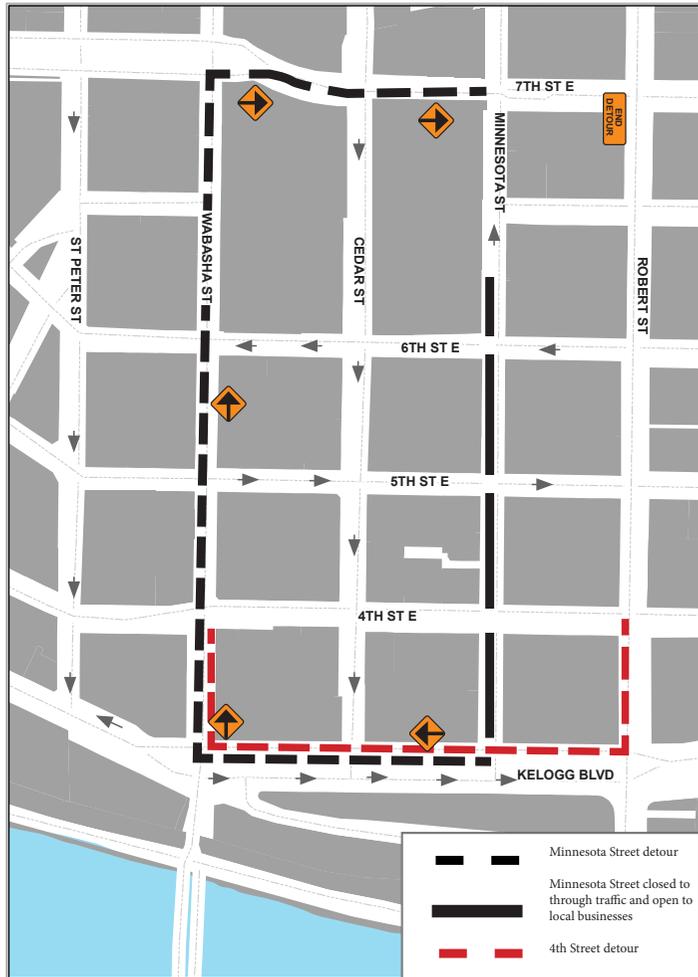

Access to local businesses on Minnesota

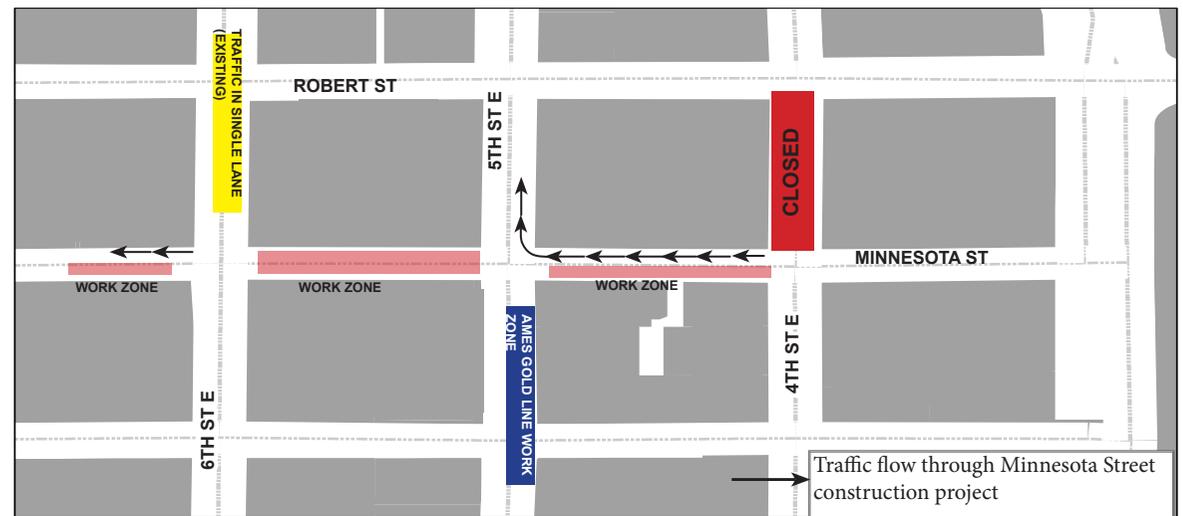

4th Street is currently closed between Minnesota Street and Robert Street



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of September 25, 2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company utility crews are working on installing storm sewer structures and piping at the Minnesota Street and 6th Street intersection.
- Veit & Company street crews are grading and shaping class 5 aggregate at the Minnesota St. and 5th Street intersection and east and west on 5th Street to the existing road connections.
- Veit & Company street crews are working on grading and shaping class 5 aggregate at the Minnesota Street and 6th Street intersection.
- Veit & Company street crews are performing removals of existing curb and gutter, sidewalk and streets at various locations at Minnesota Street in preparation for new curbing and sidewalks.
- Curb Masters is pouring concrete sidewalk and curb and gutter at Minnesota Street between 4th Street and 5th Street.
- Curb Masters poured concrete pavement at the Minnesota Street and 4th Street intersection. The crew also poured concrete pavement at the Minnesota Street and 6th Street intersection.
- Light bases and conduit were installed at Minnesota Street between 5th St. and 6th St.
- Several private utilities companies performed work on the project relocating their utility to allow for future project upgrades. These relocations are taking place at Minnesota Street between 4th Street and 6th Street.

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: **Week of September 25,2023**



What's to Expect

- Veit & Company utility crews will complete the installation of storm sewer at the Minnesota Street and 6th Street intersection.
 - Veit & Company utility crews may continue installing a tree trench located at Minnesota Street between Kellogg Boulevard and 4th Street.
 - Veit & Company street crew will work on placing class 5 aggregate base for upcoming new sidewalk at the Minnesota and 4th Street intersection.
 - Veit & Company street crew will grade and shape sub-grade for sidewalk and place class 5 aggregate at Minnesota Street and the 5th Street intersection
 - Curb Masters will pour concrete sidewalk at the Minnesota Street and 4th Street intersection.
 - Curb Masters will also pour concrete pavement at the Minnesota Street and 5th Street intersection.
 - Curb Masters will pour concrete curb and gutter at the Minnesota Street and 5th Street intersection.
 - Curb Masters will also pour concrete curb and gutter at Minnesota Street and the 6th Street intersection.
 - Private utility work will continue on the project at Minnesota Street between 4th Street and 6th Street.
 - Signal work will continue at the intersection of Minnesota and 5th Street.
-
- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.
 - We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
