


Access to local businesses on Minnesota







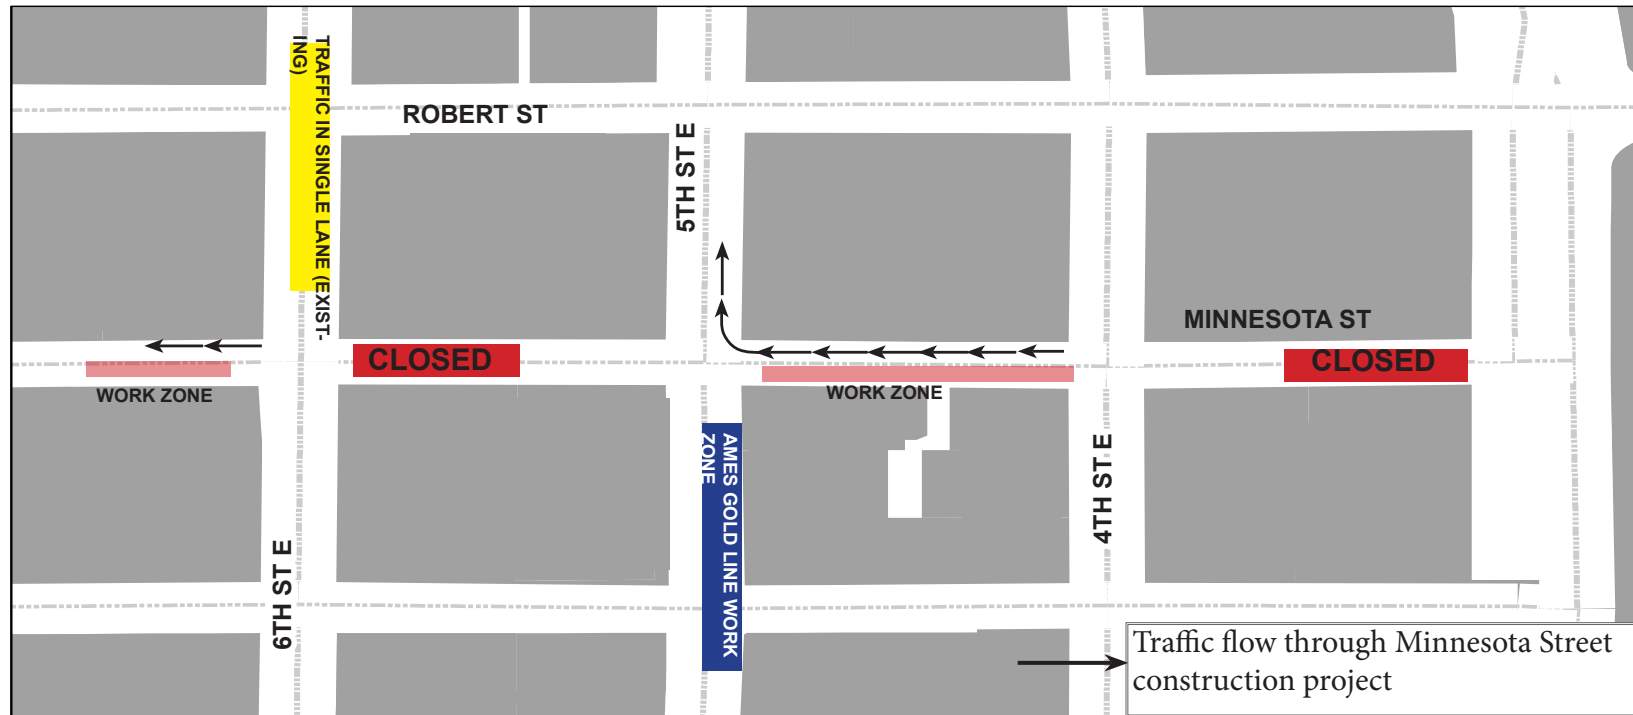



Please note that access to parking ramps at Minnesota Street between 5th Street and 6th Street are open. This section of road is two way traffic due to the closure at 6th Street.



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES:

Week of October 9, 2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company street crews are grading, shaping and placing class 5 for sidewalks at the west side of Minnesota Street from 4th Street to 5th Street.
- Veit & Company street crews placed class 5 aggregate for upcoming sidewalks at the Minnesota Street and 5th Street intersection.
- Veit & Company street crews worked on grading and shaping class 5 aggregate for new concrete pavement at the Minnesota Street and 5th Street intersection.
- Veit & Company street crew placed class 5 for bituminous pavement patching at the intersection of Minnesota Street and 5th Street.
- Veit & Company continued work on the tree trench at the west side of Minnesota Street between Kellogg Boulevard and 4th Street.
- Curb Masters is pouring concrete sidewalk at the intersection of Minnesota Street and 4th Street.
- Bituminous patching was completed at Minnesota Street and the 5th Street intersection.
- Private utilities companies worked on pulling wire in new conduits for future project upgrades. These relocations are taking place at the Minnesota Street and the 5th Street and 6th Street intersections.

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of October 9,2023



What's to Expect

- Veit & Company street crews will complete the tree trench installation at the west side of Minnesota Street between Kellogg Boulevard and 4th Street.
- Veit & Company street crews will place, grade, and shape class 5 aggregate at the Minnesota Street and 6th Street intersection for upcoming concrete pavement.
- Curb Masters will complete the sidewalk at Minnesota Street between Kellogg Boulevard and 4th Street.
- Curb Masters will also pour concrete sidewalk at the Minnesota Street and 5th Street intersection.
- Curb Masters will finish concrete curb and gutter at Minnesota Street and 6th Street.
- Curb Masters will pour concrete pavement at the Minnesota Street and 6th Street intersection.
- Private utility work will continue on the project at Minnesota Street between 5th Street and 6th Street.
- Signal work will continue at the intersection of Minnesota and 5th Street.
- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.
- We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
