


Access to local businesses on Minnesota Street







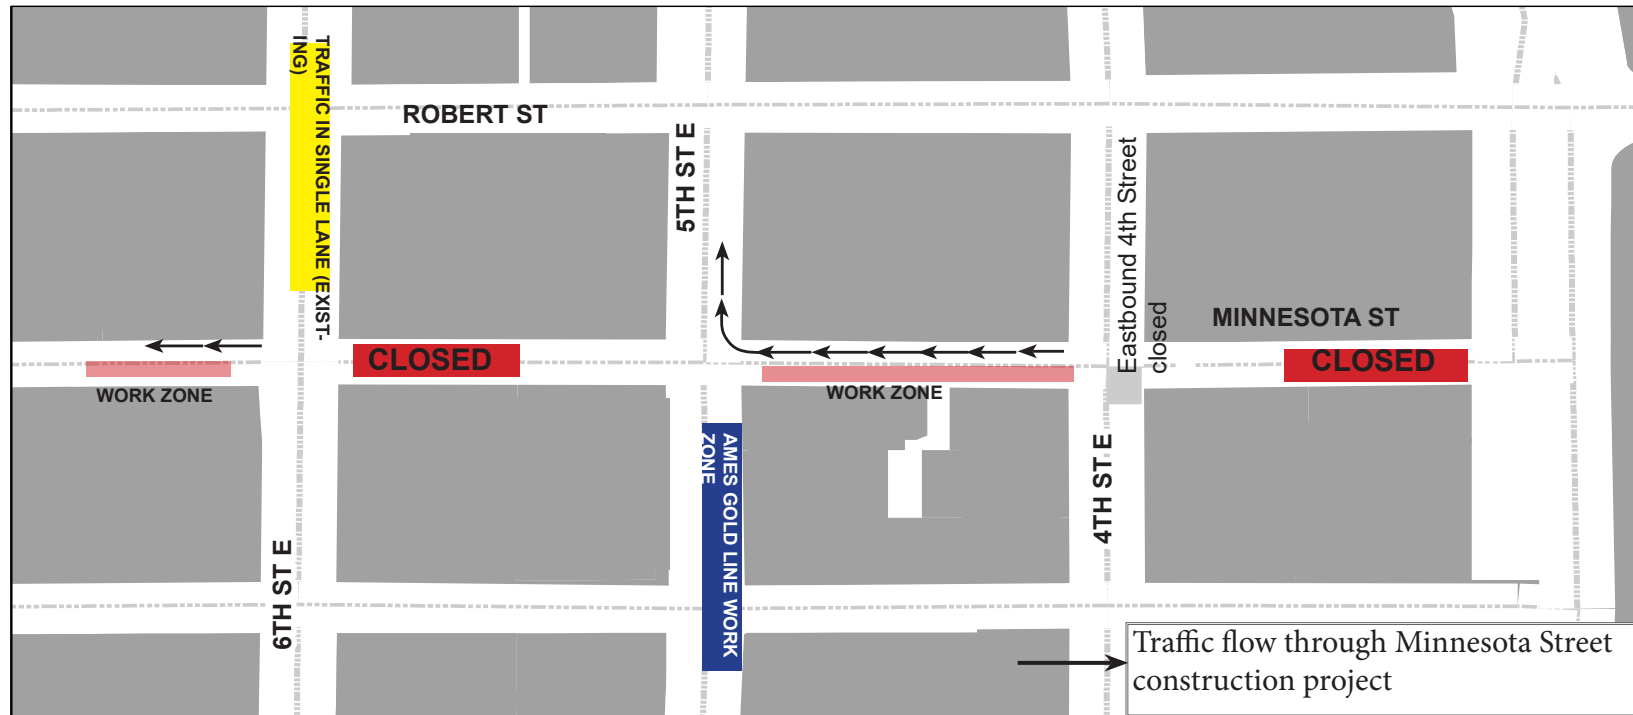



Please note that access to parking ramps at Minnesota Street between 5th Street and 6th Street are open. This section of road is two way traffic due to the closure at 6th Street.



Please also note that 4th Street going eastbound will be closed at Minnesota Street. There will be a crane at the intersection of Minnesota Street and 4th Street. East bound traffic will not be able to go east through the intersection. Westbound traffic will not be disrupted as a part of this work.

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of October 23,2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company street completed the tree trench installations at Minnesota Street between 4th Street and 6th Street.
- Veit & Company street crews placed, graded, and shaped class 5 aggregate at the Minnesota Street and 6th Street intersection for upcoming concrete pavement.
- Curb Masters completed all remaining sidewalk at Minnesota Street between Kellogg Blvd. and 4th Street. Two minor sidewalk panels will need to be poured once the temporary water main for the Kellogg Blvd. project is removed.
- Curb Masters also completed pouring concrete sidewalk at the Minnesota Street and 5th Street intersection.
- Curb Masters poured concrete pavement at the Minnesota Street and 6th Street intersection.
- A crew milled the ends of the existing pavement (at the construction limits) to allow for new bituminous pavement placement. This filled the gap between the existing bituminous pavement and the new concrete pavement.
- Private utility work continued on the project at Minnesota Street between 5th Street and 6th Street.
- Signal work will continue at the intersection of Minnesota and 5th Street and 6th Street.

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of October 23, 2023



What's to Expect

- Veit & Company street crews will install storm structure (BMP's) The first structure will be placed on 10/26/2023.
- Veit & Company will be lining manholes at Minnesota Street between Kellogg Blvd. and 6th Street.
- Curb Masters will pour concrete sidewalk at the west side of Minnesota Street between 4th Street and 5th Street.
- Curb Masters will pour concrete sidewalk at the Minnesota Street and 6th Street intersection.
- Private utility work will continue on the project at Minnesota Street between 5th Street and 6th Street.
- Signal work will continue at the intersection of Minnesota and 5th Street and 6th Street.
- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.
- We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
