


MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: 2023



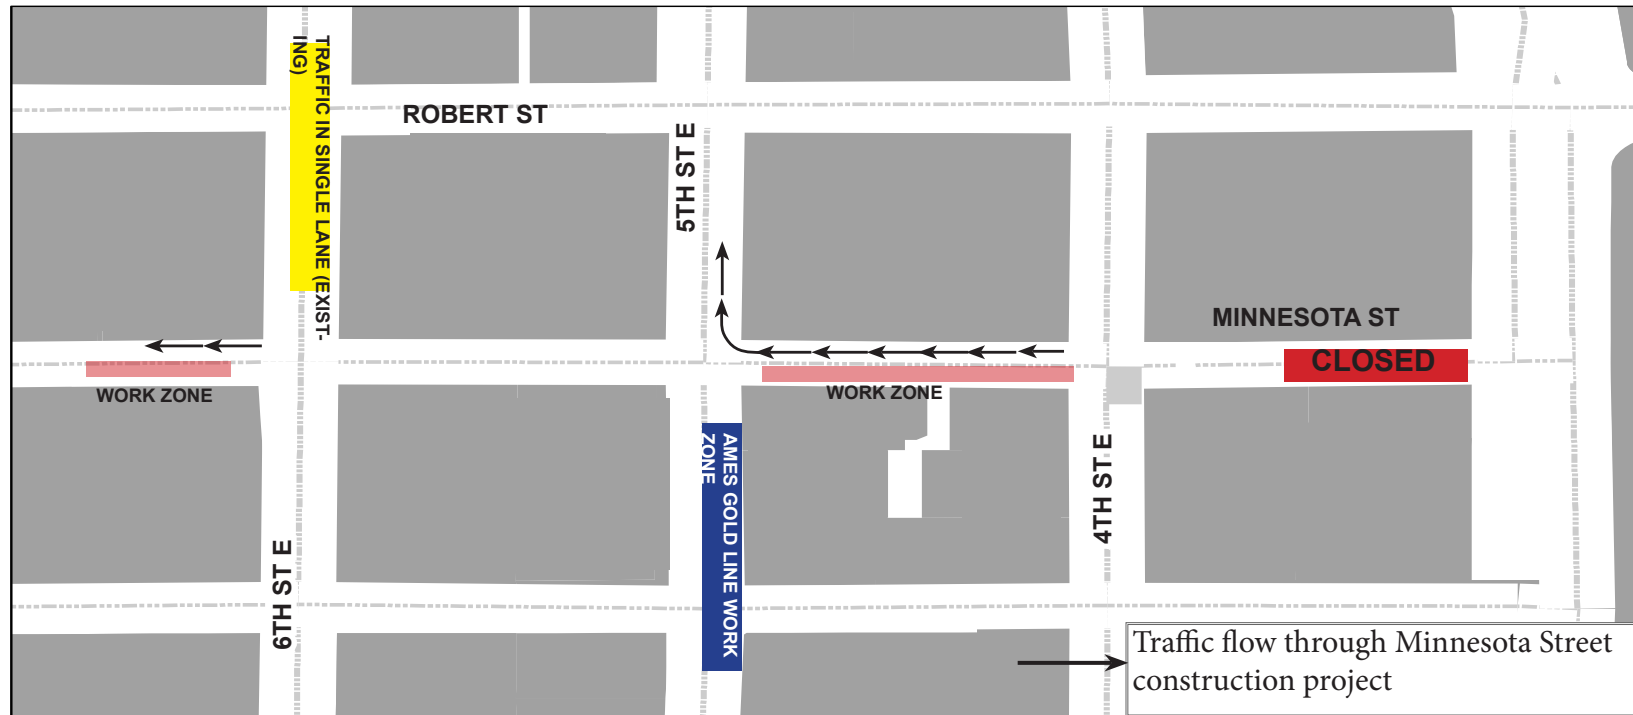

Week of November 13,

Access to local businesses on Minnesota Street



MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES:

Week of November 13, 2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

What's Happening?

- Veit & Company placed, shaped and toleranced class 5 aggregate at remaining areas that require concrete sidewalks at Minnesota Street between Kellogg Blvd. and 6th Street.
- Viet & Company placed, shaped and toleranced class 5 for the new bituminous bike trail at the west side of Minnesota Street between Kellogg Blvd. and 6th Street.
- Curb Masters poured concrete sidewalk at all open areas on Minnesota Street between Kellogg Blvd. and 6th Street.
- Curb Masters finished curb and gutter at all open areas at Minnesota Street between Kellogg Blvd. and 6th Street.
- The new bituminous trail was paved at the west side of Minnesota Street between Kellogg Blvd and 6th Street.
- Signal work will continue at the intersection of Minnesota and 5th Street and 6th Street.
- Striping of streets are expected to occur the week of November 13th.
-

MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of November 13, 2023



What's to Expect

- Veit & Company will install brick pavers at Minnesota Street and 4th Street.
- Veit will work on demobilizing from the site and completing project clean up for the winter.
- Striping of streets will take place on Minnesota Street between Kellogg Boulevard and 6th Street as well as all side streets disturbed by construction.
- Street signage will be installed at Minnesota Street between Kellogg Boulevard and 6th Street.
- Street lighting will be installed at Minnesota Street between Kellogg Boulevard and 6th Street.
- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.
- We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
