








## Access to local businesses on Minnesota Street

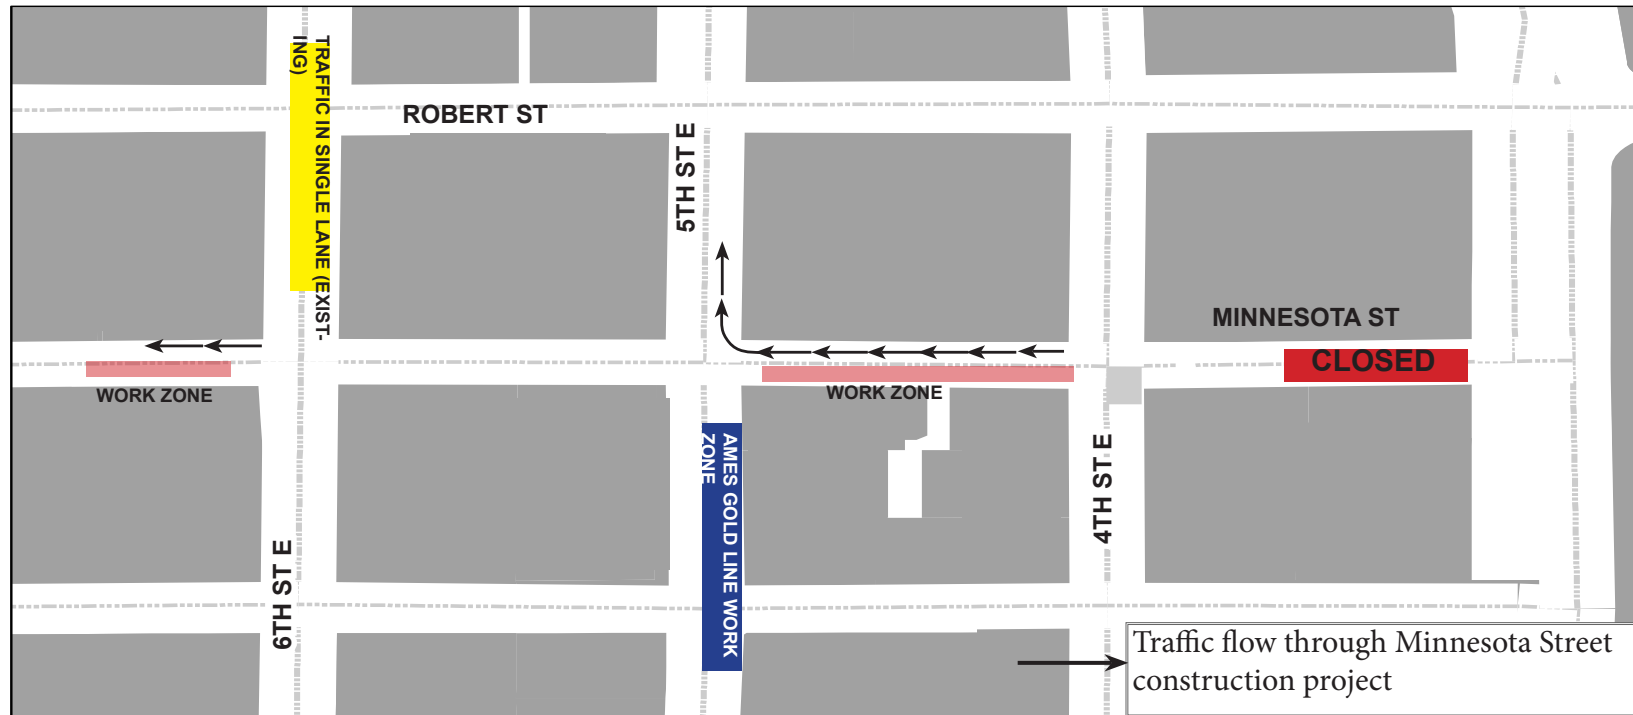

All roads are anticipated to be opened by November 10th, 2023 following striping of the streets.

# MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of November 6, 2023

Block	Anticipated Construction Activities							Notes
	Sidewalk	Road	Watermain	Storm Sewer	Signals	Removals	Underground Utilities	
7th St to 6th St								
6th St Intersection								
6th St to 5th St								
5th St Intersection								
5th St to 4th St								
4th St Intersection								
4th St to Kellogg Blvd								

## What's Happening?

- Veit & Company utility crews completed the installation of storm structure (BMP's)
- Veit & Company completed the lining of manholes at Minnesota Street between Kellogg Blvd. and 6th Street.
- Veit & Company started to place, shape and tolerance class 5 aggregate for the new bike trail at Minnesota Street between Kellogg Blvd. and 6th Street.
- Curb Masters poured concrete sidewalk at various open areas on Minnesota Street between Kellogg Blvd. and 6th Street.
- Curb Masters is working on completing the pouring of concrete curb and gutter at all open areas at Minnesota Street between Kellogg Blvd. and 6th Street.
- It is anticipated that the new bituminous trail will be paved at the west side of Minnesota Street between Kellogg Blvd and 6th Street on 11/3/2023. This may be delayed until the week of November 6th.
- Signal work will continue at the intersection of Minnesota and 5th Street and 6th Street.

# MINNESOTA STREET PHASE 1- ST. PAUL CONSTRUCTION UPDATES: Week of November 6, 2023



## What's to Expect

- Veit & Company will place, shape and tolerance class 5 aggregate at remaining areas that require concrete sidewalks at Minnesota Street between Kellogg Blvd. and 6th Street.
- Viet & Company will place, shape and tolerance class 5 for the new bituminous bike trail at the west side of Minnesota Street between Kellogg Blvd. and 6th Street. If not completed the week of October 30th.
- Curb Masters will pour concrete sidewalk at all open areas on Minnesota Street between Kellogg Blvd. and 6th Street.
- Curb Masters will finish curb and gutter at all open areas at Minnesota Street between Kellogg Blvd. and 6th Street.
- The new bituminous trail will be paved at the west side of Minnesota Street between Kellogg Blvd and 6th Street if not completed the week of October 30th.
- Signal work will continue at the intersection of Minnesota and 5th Street and 6th Street.
- Striping of streets are expected to occur the week of November 6th.
  
- Please understand that there may be times during deliveries of materials to the project and during construction activities that access may be temporarily blocked. The contractor will make sure that these disruptions are infrequent and a very short duration. The contractor will also notify businesses when these occurrences take place.
  
- We very much appreciate your patience during the construction of Minnesota Street we understand that construction can be an inconvenience.

For questions or concerns related to the Minnesota Street project, please contact Terry Campbell with Stantec at 507-512-9890. Terry is the on-site construction representative and will be happy to assist you.
